

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 1

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept



Setup Start
Stop



Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00



Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: ME Date: 09-11-09 Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start
Stop



Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	----------------	--------------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D2906	Rev B

100		0.00							
	DOCUMENT CONTROL								
DC	Memo	0.00							
Document Control	Photocopy D209-669 bluefile & type labels per PPP D205-669-043 Chg 002								

N/A *[Signature]*

110		0.00							
	Skidtubes								
Skidtubes	Memo	0.00							
Skidtubes	1- Inspect mat'l D2500-1-190 for damage 2-Cut D2500-1-190 per Dwg D2906 if necessaryDeburr ends 3-Acid etch and Alodine tube per QSI 005 4.1								

1 11/11/10

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 2

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept



Setup Start



Stop



Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00



Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start



Stop



Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

120

QC3- Inspect Part Finish

0.00



QC

Memo

0.00

Quality Control

DP 9-11-17

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM

Page 3

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept

Setup Start

Stop

Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00

Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start

Stop

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	----------------	--------------	--------------	---------------	---------------	------------------	----------------

130



Skidtubes

Skidtubes

Skidtubes

Memo

0.00

1-Drill pilot holes using drill jig DT8149, DT8711-2 & DT8711-3 (Do not use cutting fluid)

2-Open holes to 0.500" as per Dwg D2906 without cutting fluid

3-Countersink holes as per Dwg D2906 without cutting fluid

4-Deburr and blow out all chips from inside of tube

5-Bond web in place per QSI 015. Allow 12 Hrs. cure time before cutting
Pick:Qty ☐ Part Number ☐ Description ☐ Batch
A/R ☐ ☐ Sikaflex-291 ☐ M02395 ☐

Sikaflex expire date: 12/2/32

Start Time: 4:10 Date: 11/11/07

Fin Time: 8:00 AM Date: 11/11/07

pick:

Qty	P/N	description	B/N
1	D2926-3	Web	653525

Jib
09-11-17

11/11/07

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 4

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept



Setup Start



Stop



Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00



Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start



Stop



Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140 CNC Bend 1 CNC Delta 100 Bender	BENDING MACHINE - CROSSTUBES Memo 1-Bend as per program COB43FWD & COBRAFT on CNC Bender and Folio FT 2-Cut tubes as per Dwg. D2906 & per template DT8185B & DT8185BC	0.00 0.00				1		9/11/18	
150 Skidtubes Skidtubes	Skidtubes Memo 1-Cut tube as per dwg and ensure ends are perpendicular to ridge 2-Deburr ends 3-Prepare tube for welding, remove alodine as required.	0.00 0.00						MB 09-11-18	
160 QC Quality Control	QC5- Inspect part completeness to step on W/O Memo	0.00 0.00						BE 09-11-18	

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 5

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept



Setup Start
Stop



Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00



Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start
Stop



Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	----------------	--------------	--------------	---------------	---------------	------------------	----------------

170

0.00



Large Fab

Skidtubes

Memo

0.00

Skidtubes

1-Weld crossbolt spacers D2579 as per Dwg. D2906 and QSI 004.
For D2579 spacers, weld one side, pass 3/8" drill, weld other side, pass 3/8" drill
A/R□□□ Aluminum Rod *M112507* *BE 09/11/18*

2-Grind welds as per Dwg D2906 Grind flush ridge made from bending *M 9/11/19*

3-Drill holes for wearplates using DT8217 Open holes to 19/64", adjust stopper not to hit web. Debur

4-Counterbore crossbolt spacers to 7/16" ID x 1.0" deep as per Dwg D2906, Debur holes

5-Drill pilot holes for aft & fwd cap using DT8215 open holes to #6" Debur

6-Drill pilot holes for Tow ring using DT8091-3, open to .640" and Debur

180

QC10- Inspect visual per QSI004- ground welds

0.00



QC

Memo

0.00

Quality Control

2) S 02/11/20

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM

Page 6

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept

Setup Start

Stop

Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00

Cust Item ID:




Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start

Stop

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
190  QC Quality Control	QC5- Inspect part completeness to step on W/O Memo	0.00 0.00	⇒ Sordulzo			(48)	/		
200  HandFinish Hand Finishing	Pressure Wash per QSI005 4.3 Memo	0.00 0.00	⇒ M2 09/11/2011			(X1)	/		
210  Powdercoat Powder Coating	White Gloss(Ref:4.3.5.1) per QSI005 4.3-Alum M112 140 Memo START TIME: 11:30am OVEN TEMPERATURE: 320°F FINISH TIME: 12:00pm	0.00 0.00	⇒ M2 09/11/2011			(10)	/		

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 7

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept



Setup Start



Stop



Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00



Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start



Stop



Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Draw
Number

Draw
Rev.

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

220

QC3- Inspect Part Finish

0.00

BR 09-11-25

①



QC

Memo

0.00

Quality Control

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 8

Item ID: D209-669-043
Revision ID: B
Item Name: Replacement Skidtube

Accept



Setup Start



Stop



Start Date: 11/10/2009 Start Qty: 1.00
Required Date: 11/20/2009 Req'd Qty: 1.00



Cust Item ID:
Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start



Stop



Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	----------------	--------------	--------------	---------------	---------------	------------------	----------------

230

0.00



HandFinish

HandFinishing

Memo

0.00

1-Install inserts & wearplates as per Dwg. D2906. Use a drop of Sikaflex on insert holes before installing wearplates

A/R ☐ ☐ ☐ Sikaflex-291

Sikaflex expire date:

M112345
10/08

2-Coat D2594-3 O' rings with Petroleum Jelly and install on D2594-1 plugs as per Dwg D2906

3-Inspect for foreign object per QSI 024

4-Install D2855 Fwd & Aft Cap as per Dwg D2906 and seal Fwd & Aft Cap with Sikaflex. Clean excess adhesive

A/R ☐ ☐ ☐ Sikaflex-291

Sikaflex expire date:

M112345
10/08

5-Wing Walk as per Dwg D2906 and QSI 005 4.4

Batch:

M112623 => m-h 09/11/25

PR 09-11-25. ①

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 53534

November 09, 2009 8:40:21 AM



Page 9

Item ID: D209-669-043

Accept



Setup Start



Revision ID: B

Stop



Item Name: Replacement Skidtube

Start Date: 11/10/2009 Start Qty: 1.00



Cust Item ID:

Required Date: 11/20/2009 Req'd Qty: 1.00



Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start



QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop



Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Draw Number	Draw Rev.	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
240 QC Quality Control	QC5- Inspect part completeness to step on W/O Memo Inspect Aft Cap, Fwd Step and Wing Walk of work to Current Step Inspect for Foreign objects per QSI 024	0.00 28 Oct/26 0.00							
250 Packaging Packaging Packaging	Packaging Memo Identify and pack for shipping as per PPPD209-669-043 Location: _____ PPP Rev:	0.00 0.00							
260 QC Quality Control	QC21- Final Inspection - Work Order Release Memo	0.00 0.00							

09/11/26

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Page 1

Work Order ID: 53534

Parent Item: D209-669-043RevB

Parent Item Name: Replacement Skidtube





Comments:

Start Date: 11/10/2009

Required Date: 11/20/2009

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D2500-1-190RevU/R		Manufactured	No			110	Each	0.0000	1.0000			
												
						B 50166				1 11/11/16		
Ext'n -1' Beam Tube 4"												
D2926-3RevA		Manufactured	No			110	Each	1.0000	1.0000			
												
						B 53525				1 11/11/17		
Web												

Warehouse

Loc Qty

Loc Code

Location

Main Warehouse

ST

1

52066

1

D2579RevE

Manufactured

No

170

Each

615.0000

19.0000



Crossbolt Spacer

Warehouse

Loc Qty

Loc Code

Location

Main Warehouse

LG

493

51525

493

Main Warehouse

ST

122

43988

4

46434

4

46956

2

47797

9

48272

2

51314

71

51315

30

19 BE 09/11/18

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube


Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D2855RevA 		Manufactured	No			230	Each	105.0000	2.0000			
Cap												

Warehouse Loc Qty Loc Code
Location

Main Warehouse

FP6 105
50513 1
50770 4
51539 ✓ 100

2 BR09-11-25.

AN3-5A 		Purchased	No			230	Each	2,221.000	4.0000			
Bolt												

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST 2221
100188 188
105057 ✓ 2033

4 BR09-11-25.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534

Parent Item: D209-669-043RevB

Parent Item Name: Replacement Skidtube



Comments:

Start Date: 11/10/2009

Required Date: 11/20/2009

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
AN960JD10L 		Purchased	No			230	Each	5,719.000	4.0000			
Washer												

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST	5719	
101291	16	
104885	153	
105793	236	
109632 ✓	410	
110985	4904	

4 BK 09-11-25.

* ALS7-1032-130

Purchased

No

230

Each

1,880.000

44.0000



Insert

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST	1880	
105855	16	
108606	52	
111529	1488	
111779	313	
112772	11	

110511

44. BK 09-11-25.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube

Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	--------------------------	---------------	----------------	--------

AN3C4A		Purchased	No			230	Each	944.0000	44.0000			
--------	--	-----------	----	--	--	-----	------	----------	---------	--	--	--



BOLT

Warehouse	Loc Qty	Loc Code
-----------	---------	----------

Location

Main Warehouse

ST 113121

944

112314

13

112720

12

112724

3

112794

316

112829

500

112991

100

44. PR 09-11-25.

AN960C10L

Purchased

No

230

Each

3,906.000 44.0000



washer

Warehouse	Loc Qty	Loc Code
-----------	---------	----------

Location

OFFSHORE

FG

100

103585

100

Main Warehouse

ST

3806

112116

628

112612 ✓

2178

112933

1000

414 PR 09-11-25.

Dart Aerospace Ltd

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube

Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D2594-3RevC		Manufactured	No			230	Each	994.0000	14.0000			
O-Ring, 205 Skidtube												

Warehouse Loc Qty Loc Code
Location

Main Warehouse

FP 27

51613 27

Main Warehouse

ST 967

52562 ✓ 967

14 BR 09-11-25.

D2594-1RevC

Manufactured No

230

Each

585.0000

14.0000



Plug, 205 Skidtube

Warehouse Loc Qty Loc Code
Location

Main Warehouse

ST 585

42221 16

42807 92

43884 3

46435 2

51527 9

51757 ✓ 463

14 BR 09-11-25.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube



Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D3564-9RevD  Wearshoe		Manufactured	No			230	Each	31.0000	1.0000 			

<u>Warehouse</u>	<u>Loc Qty</u>	<u>Loc Code</u>
<u>Location</u>		
Main Warehouse		
FP19	29	
51675	7	
52593 ✓	22	
Main Warehouse		
ST	2	
44659	1	
45825 ~	1	

1 BL 09-11-25

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube

Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D3564-11RevD		Manufactured	No			230	Each	43.0000	1.0000			

Wearshoe

<u>Warehouse</u>	<u>Loc Qty</u>	<u>Loc Code</u>
<u>Location</u>		
Main Warehouse		
FP	10	
51905	10	
Main Warehouse		
FP19	31	
51594	8	
52125 ✓	23	
Main Warehouse		
ST	2	
45823	1	
50112	1	

1 09-11-25.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

Page 8

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube



Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D3564-5RevD  Wearshoe		Manufactured	No			230	Each	34.0000	1.0000 			

<u>Warehouse</u>	<u>Loc Qty</u>	<u>Loc Code</u>
<u>Location</u>		
OFFSHORE		
FG	2	
34806	2	
Main Warehouse		
FP19	16	
51655	8	
51925	8	
Main Warehouse		
ST	16	
45824	1	
47433	1	
52595 ✓	14	

1 OK 09-11-25.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

Page 9

November 09, 2009 8:40:20 AM

Work Order ID: 53534



Parent Item: D209-669-043RevB



Parent Item Name: Replacement Skidtube

Start Date: 11/10/2009

Required Date: 11/20/2009

Comments:

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D3566-1RevC		Manufactured	No			230	Each	20.0000	2.0000			
Gasket												

<u>Warehouse</u>	<u>Loc Qty</u>	<u>Loc Code</u>
<u>Location</u>		
Main Warehouse		
FP	15	
52512	15	
Main Warehouse		
ST	5	
46349	1	
51218	1	
51259	3	

53455

2 BR 09-11-25.

Dart Aerospace Ltd

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

November 09, 2009 8:40:20 AM

Work Order ID: 53534

Parent Item: D209-669-043RevB

Parent Item Name: Replacement Skidtube



Comments:

Start Date: 11/10/2009

Required Date: 11/20/2009

Start Qty: 1.00

Required Qty: 1.00

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Remaining Qty To Pick	Qty Issued	Date Issued	Status
D3566-5RevC 		Manufactured	No			230	Each	34.0000	1.0000 			
Gasket												

<u>Warehouse</u>	<u>Loc Qty</u>	<u>Loc Code</u>
<u>Location</u>		
Main Warehouse		
FP	10	
51929	10	
Main Warehouse		
FP19	20	
52909 ✓	20	
Main Warehouse		
ST	4	
36113	1	
46186	1	
47318	1	
51260	1	

1 BK 09-11-25.


W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries



QTY -041	QTY -043	Part Number	Description
X		D2906-041	SKIDTUBE ASSEMBLY
	X	D2906-043	SKIDTUBE ASSEMBLY
1	1	D2500-1-190	EXTRUSION
22	19	D2579	CROSS BOLT SPACER
12	14	D2594-1	PLUG
12	14	D2594-3	O-RING
2	2	D2855	AFT CAP
1		D2926-1	WEB
	1	D2926-3	WEB
1	1	D3564-9	WEARSHOE (REPLACES D2577-1)
1	1	D3564-11	WEARSHOE (REPLACES D2577-3)
1	1	D3564-5	WEARSHOE (REPLACES D2577-5)
1		D3564-15	WEARSHOE
2	2	D3566-1	GASKET
1	1	D3566-5	GASKET
1		D3566-15	GASKET
50	44	ALS7-1032-130 or AKS7-1032-130 or AKS4-1032-130 or ALS4-1032-130	INSERT
50	44	AN3C4A	BOLT
4	4	AN3-5A	BOLT
50	44	AN960C10L	WASHER
4	4	AN960JD10L	WASHER

GENERAL NOTES:

- 1) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 2) LENGTH OF D2500-1 EXTRUSION BEFORE BENDING = 190 INCHES.
- 3) INSERT D2926-1/-3 WEB TO LOCATION SHOWN OFF AFT END OF SKIDTUBE AND BOND WEB INTO OUTER TUBE WITH NON-STRUCTURAL SIKAFLEX-241/291 ADHESIVE PER DART QSI 015 BEFORE BENDING. ENSURE HOLES LINE-UP.
- 4) BEND AS A SMOOTH RADIUS STARTING WITH A MAXIMUM CENTERLINE RADIUS OF 60 AND ENDING WITH A MINIMUM RADIUS OF 30. A MAXIMUM REDUCTION OF 0.200 IN DIAMETER IS ALLOWABLE IN THE BENT PORTION OF THE TUBE.
- 5) BEND AS A SMOOTH RADIUS STARTING WITH A MAXIMUM CENTERLINE RADIUS OF 60 AND ENDING WITH A MINIMUM RADIUS OF 30. A MAXIMUM REDUCTION OF 0.200 IN DIAMETER IS ALLOWABLE IN THE BENT PORTION OF THE TUBE.
- 6) USE DART DRILL TEMPLATE DT2906-041T1 (D2906-041) OR DT2906-043T1 (D2906-043) TO LOCATE AND DRILL Ø0.297 HOLES FOR WEARSHOE INSERTS. INSTALL ALS7-1032-130 PER SECTION C-C AFTER FINISH. INSTALL AN3C4A BOLTS AND AN960C10L WASHERS WITH SIKAFLEX-241/291.
- 7) WELDING TO BE DONE PER DART QSI 004.
- 8) FINISH:
ACID ETCH, ALODINE PER DART QSI 005 4.1 PRIOR TO INSERTING D2926-1/-3 WEB. POWDER COAT ASSEMBLY WHITE (REF 4.3.5.1) PER DART QSI 005 4.3
BLACK ANTI-SKID PAINT AS INDICATED PER DART QSI 005 4.4
- 9) INSERT D2594-1 PLUG C/W D2594-3 O-RING IN HOLES MARKED 'P' (BOTH SIDES OF TUBE) AFTER FINISH (12 PLACES).
- 10) ALL DIMENSIONS ARE IN INCHES.

53534

RELEASED

07.09.04

B	UPDATE DRAWING FORMAT; RE-ORGANIZE; ADD STAINLESS STEEL WEARPLATES AND GASKETS CHANGE WEARPLATE HARDWARE TO SS; PG 1: ADD NOTE 10; PG 2 C7: REMOVE AFT Ø0.640 HOLE FROM -041; PG 3 C3: CORRECTED -043 CAP P/N; PG 3 D7: 38 PLACES WAS 44 PLACES;	CB	07.08.21
A	NEW ISSUE	CP	04.06.22
REV.	DESCRIPTION	BY	DATE
DESIGN	47	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	CB		
CHECKED	PH	DRAWING NO.	REV. B
MFG. APPR.	21	D2906	SHEET 1 OF 3
APPROVED	47	TITLE	SCALE
DE APPR.	47	AH-1 (209) SKIDTUBE ASSEMBLY	NTS
DATE	07.08.21	COPYRIGHT © 2004 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector


Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____


NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries


8 7 6 5 4 3 2 1

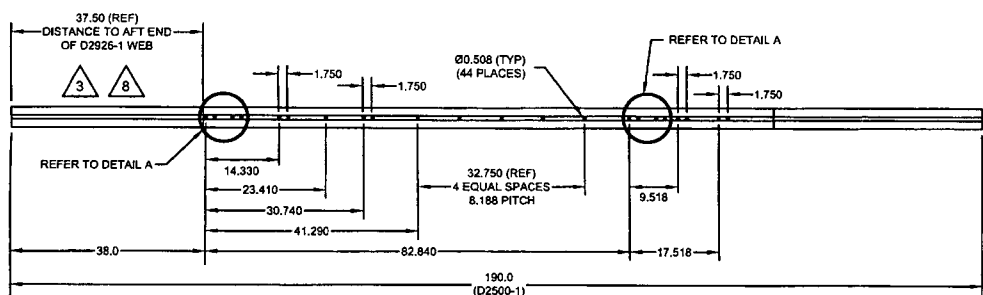


D2906-1 DRILLING DETAIL

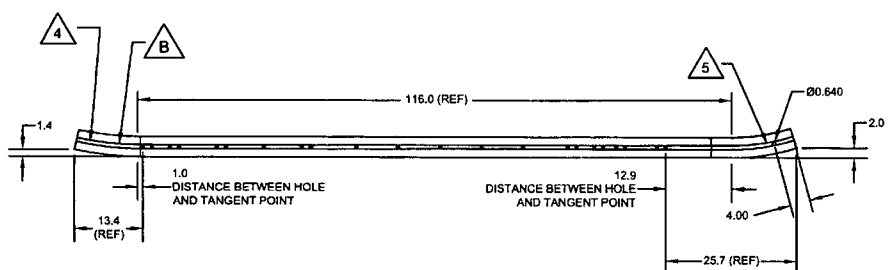


D2906-041 BENDING AND CUTTING DETAIL

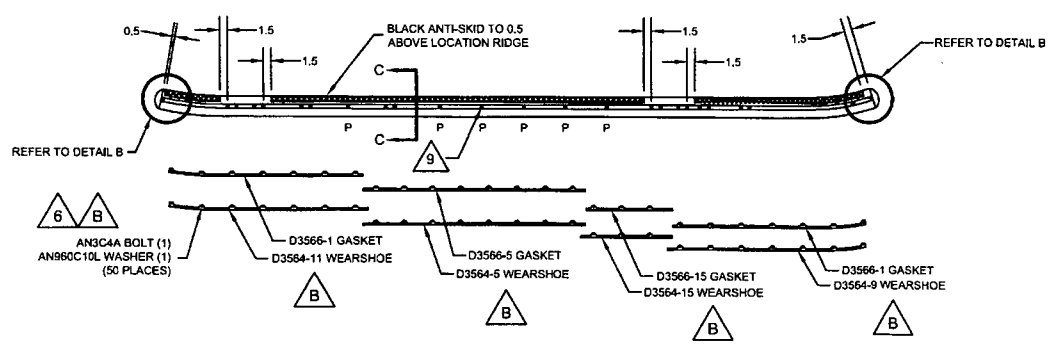

D2906-041 ASSEMBLY DETAIL

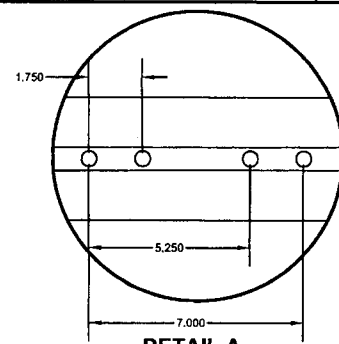


**DETAIL A
SCALE 1:4**

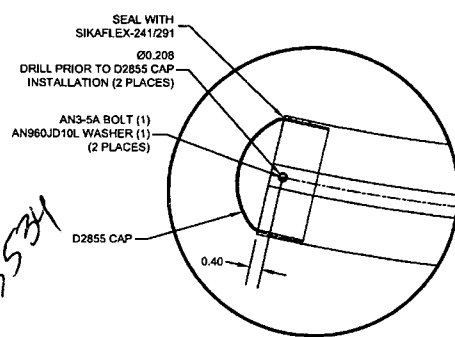

**DETAIL B
SCALE 1:4**

#53534

RELEASED
07.09.04



**SECTION C-C
SCALE 1:4**

- AFTER DRILLING AND BENDING ASSEMBLY PERFORM THE FOLLOWING FOR Ø0.508 HOLES ONLY:
1. CHAMFER HOLE 0.050 X 45°
 2. INSERT D2579 SPACER (22 PLACES)
 3. WELD INTO PLACE AND GRIND FLUSH
 4. C-BORE D2579 SPACER TO Ø0.437 X 1.00 DEEP

DESIGN	9P	DART AEROSPACE LTD	
DRAWN	CB	HAWKESBURY, ONTARIO, CANADA	
CHECKED	PH	DRAWING NO.	REV. B
MFG. APPR.	PH	D2906	SHEET 2 OF 3
APPROVED	PH	TITLE	SCALE
DE APPR.	PH	AH-1 (209) SKIDTUBE ASSEMBLY	1:24
DATE	07.08.21	COPYRIGHT © 2004 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

8 7 6 5 4 3 2 1

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries



RELEASED

07.09.24



**AFTER DRILLING AND BENDING ASSEMBLY
PERFORM THE FOLLOWING FOR Ø0.508 HOLES ONLY:**

- 1. CHAMFER HOLE 0.050 X 45°**
- 2. INSERT D2579 SPACER (22 PLACES)**
- 3. WELD INTO PLACE AND GRIND FLUSH**
- 4. BORE D2579 SPACER TO Ø0.437 X 1.00 DEEP**

DESIGN	<i>P</i>	DART AEROSPACE LTD	
DRAWN	<i>CB</i>	HAWKESBURY, ONTARIO, CANADA	
CHECKED	<i>PH</i>	DRAWING NO.	REV. B
MFG. APPR.	<i>PH</i>	D2906	SHEET 3 OF 3
APPROVED	<i>PH</i>	TITLE	SCALE
DE APPR.	<i>PH</i>	AH-1 (209) SKIDTUBE ASSEMBLY 1:24	
DATE	07.08.21	COPYRIGHT © 2004 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE LOANED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

NO. 218

AWS D17.1.2001
QUALIFICATION TEST RECORD

Name: Barclay Elliott
Job number: 5354.2
Part number: A209-669-CH3
Description: SKID tube
Welding Process: Tig[☒] Mig[☐]
Base material: Alum
Current: AC[☒] DC[☐]

TEST REQUIREMENTS AND RESULTS

Visual: pass[☒] fail[☐]
Penetration: pass[☒] fail[☐]

UNACCEPTABLE

Cracks: pass[☒] fail[☐]
Undercut: pass[☒] fail[☐]
Pin holes: pass[☒] fail[☐]
Overlap (cold lap): pass[☒] fail[☐]
Porosity (surface): pass[☒] fail[☐]
Coloration: pass[☒] fail[☐]

Qualifier David March Date of Test Coupon 09/11/20
Welder Barclay Elliott Date of Test Coupon 09/11/20

The above named individual is qualified in accordance with AWS D17.1.2001 to weld
